

Ventia – EastLink Tunnel

Ventilation Stack Air Quality Monitoring Validated Data Report 01 January 2025 to 31 March 2025

Ref: DR.2025Q1.ETL Issue Date: 1 May 2025 Report prepared by: Tim Allfrey

NATA Accredited Laboratory Number 19660

Accredited for compliance with ISO/IEC17025 – Testing

The results of the tests, calibrations and/or measurements included in this document are traceable to Australian / national standards.



Norditech Pty Ltd Unit 2/87 Station Road Seven Hills NSW 2147

1300 572 822

info@norditech.com.au norditech.com.au



Document Control

Revision	Date	Details	Prepared By	Approved By
0	1/05/2025		ТА	BN

Prepared by

Auly

Tim Allfrey 1 May 2025

Approved by



Bruno Nourdine 1 May 2025

Distribution

Format	Recipient	Details
PDF	George Vasiliadis	GVasiliadis@connecteast.com.au
PDF	Robbie Kristenson	rkristenson@connecteast.com.au





Table of Contents

1	Executive Summary	5
	1.1 Compliance to limits	5
	1.2 Summary of Results	7
2		
	2.1 Standards Compliance	
3		
4		
•	4.1 Methodology	
	4.2 Ventilation Stacks	
	4.3 Data Collection	
	4.4 Data Validation	
	4.5 Reporting and Calculations	
	4.5.1 Data Availability	
	4.5.2 Unit Conversions	
5		
0	5.1 Units and Uncertainties	
	5.2 Last Calibrations and Maintenance records	
	5.3 Automatic Instrument Calibration Checks	
6		
0	6.1 July 2024	
	6.1.1 Data Availability	
	6.1.2 Exceedances	
	6.1.3 Tabulated Results	
	6.1.3.1 Statistical Summary of 1-hour Mass Rate Data Western and Eastern Ventilation Stacks	
	6.1.4 Graphical Representations	
	6.1.4.1 July 2024 - Monthly 1-hour mass rate NO ₂	
	6.1.4.2 July 2024 - Monthly 1-hour mass rate NO	
	6.1.4.3 July 2024 - Monthly 1-hour mass rate CO	
	6.1.4.4 July 2024 - Monthly 1-hour mass rate PM _{2.5}	
	6.1.4.5 July 2024 - Monthly 1-hour mass rate PM ₁₀	
	6.1.4.6 July 2024 - Monthly 1-hour average stack velocity	
	6.1.4.7 July 2024 - Monthly 1-hour average stack temperature	
	6.1.5 Data Validation Table	
	6.1.5.1 July 2024 - Western Ventilation Stack	
	6.1.5.2 July 2024 - Eastern Ventilation Stack	
	6.2 August 2024	
	6.2.1 Data Availability	
	6.2.2 Exceedances	
	6.2.3 Tabulated Results	
	6.2.3.1 Statistical Summary of 1-hour Mass Rate Data Western and Eastern Ventilation Stacks	
	6.2.4 Graphical Representations	
	6.2.4.1 August 2024 - Monthly 1-hour mass rate NO ₂	
	6.2.4.2 August 2024 - Monthly 1-hour mass rate NO 6.2.4.3 August 2024 - Monthly 1-hour mass rate CO	
	6.2.4.3 August 2024 - Monthly 1-hour mass rate CO 6.2.4.4 August 2024 - Monthly 1-hour mass rate PM _{2.5}	
	6.2.4.5 August 2024 - Monthly 1-hour mass rate PM _{2.5}	
	6.2.4.6 August 2024 - Monthly 1-hour average stack velocity	
	6.2.4.7 August 2024 - Monthly 1-hour average stack temperature	
	6.2.5 Data Validation Table	
	6.2.5.1 August 2024 - Western Ventilation Stack	
	6.2.5.2 August 2024 - Eastern Ventilation Stack	
	6.3 September 2024	





6.3.1 Data Availability	43
6.3.2 Exceedances	
6.3.3 Tabulated Results	45
6.3.3.1 Statistical Summary of 1-hour mass rate data Western and Eastern Ventilation Stacks	s 45
6.3.4 Graphical Representations	
6.3.4.1 September 2024 - Monthly 1-hour mass rate NO2	
6.3.4.2 September 2024 - Monthly 1-hour mass rate NO	47
6.3.4.3 September 2024 - Monthly 1-hour mass rate CO	
6.3.4.4 September 2024 - Monthly 1-hour mass rate PM _{2.5}	
6.3.4.5 September 2024 - Monthly 1-hour mass rate PM ₁₀	
6.3.4.6 September 2024 - Monthly 1-hour average stack velocity	
6.3.4.7 September 2024 - Monthly 1-hour average stack temperature	
6.3.5 Data Validation Table	53
6.3.5.1 September 2024 - Western Ventilation Stack	
6.3.5.2 September 2024 - Eastern Ventilation Stack	
6.4 Data Availability Year to Date	54
6.5 Annual Performance Statement Bubble Limits	55
7 Report Summary	56
Appendix 1	
Glossary	
Data Validation Explanations	

Figures

Figure 1: EastLink Tunnel ventilation stack locations	12
Figure 2: July 2024 Monthly 1-hour mass rate NO ₂	23
Figure 3: July 2024 Monthly 1-hour mass rate NO	24
Figure 4: July 2024 Monthly 1-hour mass rate CO	25
Figure 5: July 2024 Monthly 1-hour mass rate PM _{2.5}	26
Figure 6: July 2024 Monthly 1-hour mass rate PM ₁₀	27
Figure 7: July 2024 Monthly 1-hour average stack velocity	28
Figure 8: July 2024 Monthly 1-hour average stack temperature	29
Figure 9: August 2024 Monthly 1-hour mass rate NO2	34
Figure 10: August 2024 Monthly 1-hour mass rate NO	
Figure 11: August 2024 Monthly 1-hour mass rate CO	36
Figure 12: August 2024 Monthly 1-hour mass rate PM _{2.5}	
Figure 13: August 2024 Monthly 1-hour mass rate PM ₁₀	38
Figure 14: August 2024 Monthly 1-hour average stack velocity	39
Figure 15: August 2024 Monthly 1-hour average stack temperature	40
Figure 16: September 2024 Monthly 1-hour mass rate NO2	46
Figure 17: September 2024 Monthly 1-hour mass rate NO	47
Figure 18: September 2024 Monthly 1-hour mass rate CO	
Figure 19: September 2024 Monthly 1-hour mass rate PM _{2.5}	49
Figure 20: September 2024 Monthly 1-hour mass rate PM ₁₀	50
Figure 21: September 2024 Monthly 1-hour average stack velocity	
Figure 22: September 2024 Monthly 1-hour average stack temperature	
Figure 23: Annual Performance Statement stack emission rates	55







Table 4. April 0004 Free demons of FDA Lineits	-
Table 1: April 2024 Exceedances of EPA Limits	5
Table 2: May 2024 Exceedances of EPA Limits Table 3: June 2024 Exceedances of EPA Limits	0
Table 3: June 2024 Exceedances of EPA Limits	
Table 5: May 2024 Summary of results	
Table 6: June 2024 Summary of results	
Table 7: EPA Compliance Limits	
Table 8: Measurement methods and instrumentation	
Table 9: EastLink Tunnel ventilation stack GPS Coordinates	
Table 9: EastLink Tunnel ventilation stack GPS Coordinates	
Table 11: April 2024 Instrument calibration dates	-
Table 12: May 2024 Instrument calibration dates	
Table 13: June 2024 Instrument calibration dates	17
Table 14: Nightly span, zero and CO reference times	
Table 14: Nightly span, 2ero and CO reference times	
Table 16: April 2024 Exceedances of EPA Goals	20 21
Table 10: April 2024 Exceedances of ETA Coals Table 17: April 2024 Summary of 1-hour mass rate pollutant data	
Table 18: April 2024 Western Ventilation Stack data validation	30
Table 19: April 2024 Eastern Ventilation Stack data validation	30
Table 20: May 2024 ventilation stack data availability	31
Table 21: May 2024 Exceedances of EPA Goals	
Table 22: May 2024 Summary of 1-hour mass rate pollutant data	
Table 23: May 2024 Western Ventilation Stack data validation	41
Table 24: May 2024 Eastern Ventilation Stack data validation	42
Table 25: June 2024 ventilation stack data availability	43
Table 26: June 2024 Exceedances of EPA Goals	
Table 27: June 2024 Summary of 1-hour mass rate pollutant data	
Table 28: June 2024 Western Ventilation Stack data validation	
Table 29: June 2024 Eastern Ventilation Stack data validation	
Table 30: EastLink Ventilation Stack year to date data availability	
Table 31: Annual Performance Statement stack emission rates	





1 Executive Summary

EastLink is a 39 km motorway running between Nunawading and Frankston, linking the Eastern, Monash Frankston and Peninsula Link freeways. Two 1.6 km tunnels pass under the Mullum Mullum Valley, with a ventilation stack at the end of each tunnel as an exit point for tunnel ventilation.

Two ventilation stacks provide ventilation for the tunnel, one at the western end of the tunnel at Discharge Point 1 (DP1), and one at the eastern end of the tunnel at Discharge Point 2 (DP2).

This report presents the monthly validated stack data for January 2025 to March 2025 to Ventia Pty Ltd for the EastLink Tunnel.

1.1 Compliance to limits

The Environment Protection Authority (Victoria) designates limits to which pollutant mass rates being discharged from the ventilation stacks must meet. (Environmental Licence No. 2043).

Instances of the ventilation stack pollutants exceeding the EPA Limits goals during the reporting period are presented in Table 1, Table 2 and Table 3 and below. Maximum mass rates are provided for comparison to the limits.

EastLink Ventiliation Stack Air Quality Limit Exceedances January 2025											
Location	Parameter	Time Period	Licence Limit	Units	Maximum Mass Rate	Number of exceedances	Value of exceedance	Date and Time of exceedance			
	NO ₂	1-hour	3.98	kg/h	0.41	-	-	-			
Western Ventilation	со	1-hour	112	kg/h	4.79	-	-	-			
Stack (Discharge Point 1)	PM _{2.5}	1-hour	2.4	kg/h	0.15	-	-	-			
i oinc i)	PM ₁₀	1-hour	2.6	kg/h	0.76	-	-	-			
	NO ₂	1-hour	3.98	kg/h	0.89	-	-	-			
Eastern Ventilation	со	1-hour	112	kg/h	5.66	-	-	-			
Stack (Discharge Point 2)	PM _{2.5}	1-hour	2.4	kg/h	0.15	-	-	-			
	PM ₁₀	1-hour	2.6	kg/h	0.50	-	-	-			

There were nil exceedances of the prescribed limits during the reporting period.

Table 1: January 2025 Exceedances of EPA Limits





EastLink Ventiliation Stack Air Quality Limit Exceedances February 2025											
Location	Parameter	Time Period	Licence Limit	Units	Maximum Mass Rate	Number of exceedances	Value of exceedance	Date and Time of exceedance			
	NO ₂	1-hour	3.98	kg/h	0.39	-	-	-			
Western Ventilation Stack	со	1-hour	112	kg/h	5.50	-	-	-			
(Discharge Point 1)	PM _{2.5}	1-hour	2.4	kg/h	0.21	-	-	-			
T On (CT)	PM ₁₀	1-hour	2.6	kg/h	0.82	-	-	-			
Frater	NO ₂	1-hour	3.98	kg/h	0.96	-	-	-			
Eastern Ventilation Stack	со	1-hour	112	kg/h	6.82	-	-	-			
(Discharge Point 2)	PM _{2.5}	1-hour	2.4	kg/h	0.16	-	-	-			
	PM ₁₀	1-hour	2.6	kg/h	0.75	-	-	-			

Table 2: February 2025 Exceedances of EPA Limits

EastLink Ventiliation Stack Air Quality Limit Exceedances March 2025											
Location	Parameter	Time Period	Licence Limit	Units	Maximum Mass Rate	Number of exceedances	Value of exceedance	Date and Time of exceedance			
10/	NO2	1-hour	3.98	kg/h	0.41	-	-	-			
Western Ventilation Stack	со	1-hour	112	kg/h	5.50	-	-	-			
(Discharge Point 1)	PM _{2.5}	1-hour	2.4	kg/h	0.30	-	-	-			
T On (CT)	PM ₁₀	1-hour	2.6	kg/h	0.82	-	-	-			
Fraters	NO ₂	1-hour	3.98	kg/h	0.98	-	-	-			
Eastern Ventilation Stack	со	1-hour	112	kg/h	6.51	-	-	-			
(Discharge Point 2)	PM _{2.5}	1-hour	2.4	kg/h	0.20	-	-	-			
Point 2)	PM ₁₀	1-hour	2.6	kg/h	0.48	-	-	-			

Table 3: March 2025 Exceedances of EPA Limits





1.2 Summary of Results

Summaries of the ventilation stack pollutants for the reporting period are presented in Table 4, Table 5 and Table 6 below. Maximum mass rates are provided for comparison to the limits.

EastLink Ventilation Stack Summary January 2025										
Location	Parameter	1hr Average Maximum	1 hr Average Minimum	Monthly Average	Monthly Total	Number of Exceedances	Data Availability (%)			
	NO (kg/h)	2.30	0.00	0.41	291.69	N/A	95.3%			
	NO ₂ (kg/h)	0.41	0.00	0.09	61.71	0	95.3%			
Western Ventilation Stack	CO (kg/h)	4.79	0.00	1.28	910.62	0	95.3%			
	PM _{2.5} (kg/h)	0.2	0.0	0.0	20.1	0	99.9%			
	PM ₁₀ (kg/h)	0.8	0.0	0.1	38.8	0	100.0%			
	NO (kg/h)	3.21	0.00	0.63	441.25	N/A	94.1%			
	NO ₂ (kg/h)	0.89	0.00	0.15	102.82	0	94.1%			
Eastern Ventilation Stack	CO (kg/h)	5.66	0.00	1.11	779.92	0	94.1%			
	PM _{2.5} (kg/h)	0.2	0.0	0.0	22.1	0	99.9%			
	PM ₁₀ (kg/h)	0.5	0.0	0.1	52.3	0	100.0%			

Table 4: January 2025 Summary of results





EastLink Ventilation Stack Summary February 2025										
Location	Parameter	1hr Average Maximum	1 hr Average Minimum	Monthly Average	Monthly Total	Number of Exceedances	Data Availability (%)			
	NO (kg/h)	2.62	0.00	0.57	330.67	N/A	87.1%			
	NO ₂ (kg/h)	0.39	0.00	0.10	60. <mark>9</mark> 2	0	87.1%			
Western Ventilation Stack	CO (kg/h)	5.50	0.00	1.56	1000.49	0	95.2%			
	PM _{2.5} (kg/h)	0.2	0.0	0.0	24.9	0	98.5%			
	PM ₁₀ (kg/h)	0.8	0.0	0.1	52.6	0	99.4%			
	NO (kg/h)	3.63	0.00	0.84	531.44	N/A	93.9%			
	NO ₂ (kg/h)	0.96	0.00	0.19	119.56	0	93.9%			
Eastern Ventilation Stack	CO (kg/h)	6.82	0.00	1.45	896.08	0	95.2%			
	PM _{2.5} (kg/h)	0.2	0.0	0.0	26.6	0	98.5%			
	PM ₁₀ (kg/h)	0.7	0.0	0.1	62.6	2	99.4%			

Table 5: February 2025 Summary of results

EastLink Ventilation Stack Summary March 2025										
Location	Parameter	1hr Average Maximum	1 hr Average Minimum	Monthly Average	Monthly Total	Number of Exceedances	Data Availability (%)			
	NO (kg/h)	2.38	0.00	0.53	379.24	N/A	95.7%			
	NO ₂ (kg/h)	0.41	0.00	0.09	66.25	0	95.7%			
Western Ventilation Stack	CO (kg/h)	5.50	0.00	1.58	1127.98	0	95.7%			
	PM _{2.5} (kg/h)	0.3	0.0	0.0	20.5	0	91.8%			
	PM ₁₀ (kg/h)	0.8	0.0	0.1	53.5	0	100.0%			
	NO (kg/h)	3.73	0.00	0.78	551.99	N/A	95.3%			
	NO ₂ (kg/h)	0.98	0.00	0.17	120.48	0	95.3%			
Eastern Ventilation Stack	CO (kg/h)	6.51	0.00	1.53	1086.07	0	95.3%			
	PM _{2.5} (kg/h)	0.2	0.0	0.0	25.7	0	96.0%			
	PM ₁₀ (kg/h)	0.5	0.0	0.1	64.9	0	100.0%			

Table 6: March 2025 Summary of results





2 Compliance Limits

Air quality limits are provided in Condition LI_DA1.13 of the Environment Protection Authority (Victoria) Licence No 2043 for the EastLink Tunnel. The air quality limits for 1-hour mass rates are shown in Table 7 below.

EastLink Ventiliation Stack Air Quality Limits									
Location	Parameter	ameter Time Period License Limit Unit		Units	Applicable Licence				
	NO ₂	1-hour	3.98	kg/h					
Western Ventilation Stack	СО	1-hour	112	kg/h	EPA Vic				
(Discharge Point 1)	PM _{2.5}	1-hour	2.4	kg/h	Licence No 2043				
	PM ₁₀	1-hour	2.6	kg/h					
	NO ₂	1-hour	3.98	kg/h					
Eastern Ventilation Stack	СО	1-hour	112	kg/h	EPA Vic				
(Discharge Point 2)			2.4	kg/h	Licence No 2043				
	PM ₁₀	1-hour	2.6	kg/h					

Table 7: EPA Compliance Limits

The procedure for reporting particulate matter results from the TEOMs and assessment of licence compliance is detailed in the EastLink Particulate Matter Protocol (PMP) dated 17/06/2013. The PMP requires validated uncorrected TEOM one hour clock average data to be compared to the following TEOM mass rate compliance limits for both DP1 and DP2.

- PM_{2.5}: 2.0 kg/h
- PM₁₀: 2.0 kg/h

2.1 Standards Compliance

Norditech's NATA Accreditation does not cover the following parameters monitored at the EastLink Tunnel ventilation stack air quality monitoring stations.

- Measurement of Stack Flow.
- AS/NZS 3580.9.8 refers specifically to the monitoring of PM₁₀.





3 Introduction

Norditech were contracted by Ventia Pty Ltd in August 2021 to provide continuous stack air quality monitoring and reporting services for the EastLink Tunnel. Ventia Pty Ltd are responsible for the operation and maintenance of the motorway.

Norditech is a NATA accredited organisation (Accreditation Number 19660).

Addresses of relevant parties:

Norditech Pty Ltd 2/87 Station Rd Seven Hills NSW 2147 Ventia Pty Ltd 2 Hillcrest Avenue Ringwood VIC 3134

This report presents the validated Western and Eastern ventilation stack data for January 2025 to March 2025.

- Describes air quality measurements.
- Reports any readings above the relevant EPA Limits.
- Compares monitoring results.
- Has been quality assured.





4 Explanation of Monitoring

4.1 Methodology

In the tunnel air is discharged via two ventilation stacks – one located at the Western end of the tunnel (DP1), and one located at the Eastern end (DP2). For each stack, monitoring as per the requirements of EPA Licence 2043 is undertaken.

Gaseous parameters are sampled by an extractive sampling system. Oxides of nitrogen are measured using chemiluminescence. Carbon monoxide is measured using non-dispersive infra-red absorption.

Particulates PM₁₀ and PM_{2.5} are measured using tapered element oscillating microbalances.

Stack gas velocity is measured using an optical flow sensor.

Monthly routine maintenance is undertaken by Norditech. Maintenance is performed as per the relevant Australian Standard or in house method. Maintenance cycles generally involve 1, 3, 6 and 12 monthly scheduled items.

The following instrumentation and methods are used in data collection:

EastLink Ventilation Stack Measurement Methods							
Parameter	Method	Instrument					
со	In house method TP.003	Thermo Scientific 48i					
NO, NO_2, NO_x	In house method TP.001	Thermo Scientific 42i					
	AS/NZS 3580.9.8						
PM ₁₀	In house method TP.005	Rupprecht & Patashnick TEOM					
	AS 4323.1						
DM	In house method TP.026						
PM _{2.5}	AS 4323.1	Rupprecht & Patashnick TEOM					
Temperature	In house method TP.012	PT100					
Stack Velocity	USEAP (CFR 40) Part 75	OSI OFS2000					

Table 8: Measurement methods and instrumentation





4.2 Ventilation Stacks

The locations of the EastLink Tunnel Western and Eastern ventilation stacks are detailed in Table 9 and Figure 1 below.

EastLink Ventilation Stack Locations						
Discharge Point Site Name		GPS Coordinates				
1	Western Ventilation Stack	-37.801229°, 145.196092°				
2	Eastern Ventilation Stack	-37.808885°, 145.212012°				

Table 9: EastLink Tunnel ventilation stack GPS Coordinates



Figure 1: EastLink Tunnel ventilation stack locations

:





4.3 Data Collection

At each Air Quality Monitoring Station, data is logged to an EnviDAS data logger at 1 minute average intervals. Each 1-minute average is calculated from data sampled at 10 second intervals.

Data is transferred automatically to Norditech's data collection software via a TCP/IP link over 4G cellular network, at a frequency of not less than 1-hour. Two datasets are maintained by Norditech, one for data validation and reporting purposes, and a non-validated data set for reference purposes.

4.4 Data Validation

Data validation is performed as per Norditech's data validation procedure TP.022. The data validation process identifies any data that is deemed not to be valid. This data is flagged as invalid in the database and is removed from the reported data.

Data may be deemed invalid for several reasons, including but not limited to:

- Instrument fault.
- Instrument calibration out of tolerance.
- Maintenance activities.

For further details and explanations of reasons for invalidating data, please refer to Appendix 1 – Data Validation Explanations.

Initial visual inspection of data is performed by inspection of graphs to identify any anomalies in the data set.

Site visit logs and maintenance and calibration certificates are cross referenced to the data set and any data affected by maintenance activities are flagged.

Instrument drift and calibration tolerances are checked, and data flagged in the database as necessary as per NATA compliance requirements.





4.5 Reporting and Calculations

All calculations and averages are calculated from 1 minute average base data and are reported as 'end time' when the averaging periods of eight hours or less. IE the average data for 01:00 is the data from 00:00 through to 01:00. One-hour averages are calculated based on a clock hour. One day averages are calculated based on calendar days. All averages are based on a minimum of 75% valid readings within the averaging period.

All data is reported at Australian Eastern Standard Time.

Validated data for Quarter 1 Month 1 is presented in the Excel workbook named "202501 EastLink Q1M1 Validated data.xlsx"

The workbooks each consist of the following sheets:

Sheet 1: Cover Sheet 2: M1 Data kg1h – Hourly data in kg/h Sheet 3: M1 Data g5m – 5-minute data in grams/5m Sheet 4: M1 Data mgm3 1h – 1-hour data in mg/m³ Sheet 5: M1 Data mgm3 5m – 5-minute data in mg/m³ Sheet 6: Eastern Validation Data Sheet 7: Western Validation Data

Validated data for Quarter 1 Month 2 is presented in the Excel workbook named "202502 EastLink Q1M2 Validated data.xlsx"

The workbooks each consist of the following sheets:

Sheet 1: Cover Sheet 2: M2 Data kg1h – Hourly data in kg/h Sheet 3: M2 Data g5m – 5-minute data in grams/5m Sheet 4: M2 Data mgm3 1h – 1-hour data in mg/m³ Sheet 5: M2 Data mgm3 5m – 5-minute data in mg/m³ Sheet 6: Eastern Validation Data Sheet 7: Western Validation Data

Validated data for Quarter 1 Month 3 is presented in the Excel workbook named "202503 EastLink Q1M3 Validated data.xlsx"

The workbook consists of the following sheets:

Sheet 1: Cover Sheet 2: M3 Data kg1h – Hourly data in kg/h Sheet 3: M3 Data g5m – 5-minute data in grams/5m Sheet 4: M3 Data mgm3 1h – 1-hour data in mg/m³ Sheet 5: M3 Data mgm3 5m – 5-minute data in mg/m³ Sheet 6: Eastern Validation Data Sheet 7: Western Validation Data





4.5.1 Data Availability

Data availability refers to the amount of available 1-hour data for the reporting period. Data availability is calculated using the following formula:

 $Data availability \% = \frac{sum of available data points}{sum of possible data points} * 100$

Where:

- Sum of available data points is the number of validated 1-hour average data points for the reporting period.
- Sum of possible data points is the number of theoretically available 1-hour data points for the reporting period.

4.5.2 Unit Conversions

Stack velocity readings are converted to flow rate using the following stack areas:

- Western Stack area 35 m²
- Eastern Stack area 35 m²

Pollutant and flow data are reported at actual conditions.





5 Calibrations and Maintenance

5.1 Units and Uncertainties

EastLink Ventilation Stack Instrument Units and Uncertainties								
Parameter	Units	Resolution	Uncertainty	Measurement Range				
со	mg/m ³	0.01	± 8.2% of reading at 62.5mg/m ³ (k=1.96)	0 to 200				
NO	mg/m ³	0.01	± 8.1% of reading for range 25.7 – 32.8mg/m ³ (k=1.96)	0 to 150				
NO ₂	mg/m ³	0.01	± 8.5% of reading at 25.7mg/m ³ (k=1.96)	0 to 150				
NO _x	mg/m ³	0.01	± 8.1% of reading for range 25.7 – 32.8mg/m ³ (k=1.96)	0 to 150				
PM ₁₀	µg/m³	0.1	±5.0 μg/m ³ or 3.6% of reading, whichever is the greater. K factor of 1.96	0 to 5000				
PM _{2.5}	µg/m³	0.1	±5.0 μg/m ³ or 3.6% of reading, whichever is the greater. K factor of 1.96	0 to 5000				
Temperature	°C	0.1	±2.0 °C ¹	-25 to 105				
Stack Velocity	m/s	1	±0.1 m/s ¹	-40 to +40				

¹ Manufacturer's stated accuracy

Table 10: Measurement units and uncertainties





5.2 Last Calibrations and Maintenance records

Instrumentation maintenance and last calibration dates are provided in Table 11, Table 12 and Table 13 below:

EastLink Ventilation Stack Maintenance and Calibrations January 2025								
Location	Parameter	Date of last scheduled maintenance	Maintenance type	Date of last calibration				
	CO	14/01/2025	1 Monthly	14/01/2025				
Western	NO, NO ₂	14/01/2025	1 Monthly	14/01/2025				
Ventilation	PM ₁₀	18/12/2024	6 Monthly	18/12/2024				
Stack (Discharge	PM _{2.5}	18/12/2024	6 Monthly	18/12/2024				
Point 1)	Stack Velocity	20/08/2024	12 Monthly	20/08/2024				
	Stack Temperature	18/12/2024	6 Monthly	25/06/2024				
	CO	14/01/2025	1 Monthly	14/01/2025				
Eastern	NO, NO ₂	14/01/2025	1 Monthly	14/01/2025				
Ventilation	PM ₁₀	18/12/2024	6 Monthly	18/12/2024				
Stack (Discharge	PM _{2.5}	18/12/2024	6 Monthly	18/12/2024				
Point 2)	Stack Velocity	22/08/2024	12 Monthly	22/08/2024				
	Stack Temperature	18/12/2024	6 Monthly	27/06/2024				

Table 11: January 2025 Instrument calibration dates

EastLink Ventilation Stack Maintenance and Calibrations February 2025								
Location	Parameter	Date of last scheduled maintenance	Maintenance type	Date of last calibration				
	CO	7/02/2025	1 Monthly	7/02/2025				
Western	NO, NO ₂	7/02/2025	1 Monthly	7/02/2025				
Ventilation Stack	PM ₁₀	18/12/2024	6 Monthly	18/12/2024				
(Discharge	PM _{2.5}	18/12/2024	6 Monthly	18/12/2024				
Point 1)	Stack Velocity	20/08/2024	12 Monthly	20/08/2024				
,	Stack Temperature	18/12/2024	6 Monthly	25/06/2024				
	CO	7/02/2025	1 Monthly	7/02/2025				
Eastern	NO, NO ₂	7/02/2025	1 Monthly	7/02/2025				
Ventilation	PM ₁₀	18/12/2024	6 Monthly	18/12/2024				
Stack (Discharge	PM _{2.5}	18/12/2024	6 Monthly	18/12/2024				
Point 2)	Stack Velocity	22/08/2024	12 Monthly	22/08/2024				
,	Stack Temperature	18/12/2024	6 Monthly	27/06/2024				

Table 12: February 2025 Instrument calibration dates





EastLink Ventilation Stack Maintenance and Calibrations March 2025								
Location	Parameter	Date of last scheduled maintenance	Maintenance type	Date of last calibration				
	CO	11/03/2025	3 Monthly	11/03/2025				
Western	NO, NO ₂	11/03/2025	3 Monthly	11/03/2025				
Ventilation Stack	PM ₁₀	5/03/2025	3 Monthly	18/12/2024				
(Discharge	PM _{2.5}	5/03/2025	3 Monthly	5/03/2025				
Point 1)	Stack Velocity	20/08/2024	12 Monthly	20/08/2024				
· · · · ·	Stack Temperature	18/12/2024	6 Monthly	25/06/2024				
	CO	11/03/2025	3 Monthly	11/03/2025				
Eastern	NO, NO ₂	11/03/2025	3 Monthly	11/03/2025				
Ventilation Stack	PM ₁₀	11/03/2025	3 Monthly	18/12/2024				
(Discharge	PM _{2.5}	11/03/2025	3 Monthly	18/12/2024				
Point 2)	Stack Velocity	22/08/2024	12 Monthly	22/08/2024				
· · · · ·	Stack Temperature	18/12/2024	6 Monthly	27/06/2024				

Table 13: March 2025 Instrument calibration dates





5.3 Automatic Instrument Calibration Checks

Table 14 below identifies the times at which the daily gaseous parameter automatic span and zero checks are performed.

This data is removed from the dataset, however, are not included in the data validation tables of data.

Nightly span and zero times for NO, NO $_2$ and CO							
Location	Parameter	Span / Zero cycle time					
Western (to	CO	00:00 - 00:34					
25/07/2024)	NO, NO ₂	01:00 - 01:44					
Western (from	CO	01:00 - 01:44					
26/07/2024)	NO, NO_2	01:00 - 01:44					
Eastern	CO	01:34 - 02:13					
Eastern	NO, NO ₂	01:34 - 02:13					

Table 14: Nightly span, zero and CO reference times.





6 Results

6.1 January 2025

6.1.1 Data Availability

Data availability for the in the ventilation stack parameters are provided in Table 15 below. For further information on data availability please refer to section 6.1.5.

EastLink Ventilation Stack Data Availability January 2025										
Station		NO	NO ₂	со	PM _{2.5}	PM ₁₀	Stack Velocity	Stack Temp.		
	Data Availability	<mark>9</mark> 5.3%	95.3%	95.3%	99.9%	100.0%	100.0%	100.0%		
Western	Collected Periods	709.0	709.0	709.0	743.0	744.0	744.0	744.0		
	Available Periods	744.0	744.0	744.0	744.0	744.0	744.0	744.0		
	Data Availability	94.1%	94.1%	94.1%	99.9%	100.0%	100.0%	100.0%		
Eastern	Collected Periods	700.0	700.0	700.0	743.0	744.0	744.0	744.0		
	Available Periods	744.0	744.0	744.0	744.0	744.0	744.0	744.0		

Table 15: January 2025 ventilation stack data availability





6.1.2 Exceedances

Instances of the ventilation stack pollutants exceeding the EPA Limits goals during the reporting period are presented in Table 16 below. Maximum mass rates are provided for comparison to the limits.

EastLink Ventiliation Stack Air Quality Limit Exceedances January 2025									
Location	Parameter	Time Period	Licence Limit	Units	Maximum Mass Rate	Number of exceedances	Value of exceedance	Date and Time of exceedance	
Mantana	NO ₂	1-hour	3.98	kg/h	0.41	-	-	-	
Western Ventilation Stack	со	1-hour	112	kg/h	4.79	-	-	-	
(Discharge Point 1)	PM _{2.5}	1-hour	2.4	kg/h	0.15	-	-	-	
T On (CT)	PM ₁₀	1-hour	2.6	kg/h	0.76	-	-	-	
Frater	NO ₂	1-hour	3.98	kg/h	0.89	-	-	-	
Eastern Ventilation	СО	1-hour	112	kg/h	5.66	-	-	-	
Stack (Discharge Point 2)	PM _{2.5}	1-hour	2.4	kg/h	0.15	-	-	-	
Point 2)	PM ₁₀	1-hour	2.6	kg/h	0.50	-	-	-	

There were nil exceedances of the prescribed limits during the reporting period.

Table 16: January 2025 Exceedances of EPA Goals





6.1.3 Tabulated Results

6.1.3.1 Statistical Summary of 1-hour Mass Rate Data Western and Eastern Ventilation Stacks

Table 17 presents 1-hour mass rate statistical data for the Western and Eastern ventilation stacks.

1-hour mass rates are calculated from 1 minute average data.

EastLink Ventilation Stack Summary January 2025									
Location	Parameter	Maximum	99 th Percentile	98 th Percentile	95 th Percentile	90 th Percentile	75 th Percentile	50 th Percentile	
	NO (kg/h)	2.30	2.06	1.81	1.24	0.98	0.65	0.34	
	NO ₂ (kg/h)	0.41	0.33	0.28	0.23	0.19	0.14	0.09	
Western Ventilation Stack	CO (kg/h)	4.79	3.86	3.59	3.18	2.68	2.12	1.51	
	PM _{2.5} (kg/h)	0.2	0.1	0.1	0.1	0.1	0.0	0.0	
	PM ₁₀ (kg/h)	0.8	0.4	0.3	0.2	0.1	0.1	0.0	
	NO (kg/h)	3.21	2.63	2.45	2.04	1.69	1.07	0.46	
	NO ₂ (kg/h)	0.89	0.63	0.57	0.46	0.35	0.24	0.13	
Eastern Ventilation Stack	CO (kg/h)	5.66	4.30	3.68	3.04	2.44	1.89	1.18	
	PM _{2.5} (kg/h)	0.2	0.1	0.1	0.1	0.1	0.1	0.0	
	PM ₁₀ (kg/h)	0.5	0.3	0.3	0.2	0.2	0.1	0.1	

Table 17: January 2025 Summary of 1-hour mass rate pollutant data





6.1.4 Graphical Representations

The following charts present 1-hour mass rate data for NO, NO₂, CO, PM_{2.5}, PM₁₀ and Stack Velocity for the Western and Eastern ventilation stacks.

1-hour mass rates are calculated from 1 minute average data.

6.1.4.1 January 2025 - Monthly 1-hour mass rate NO₂

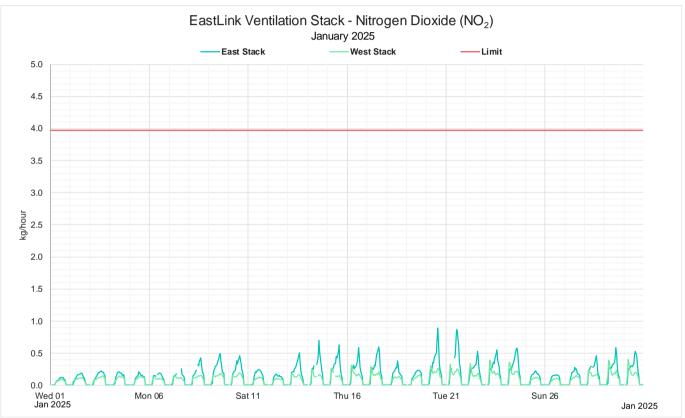


Figure 2: January 2025 Monthly 1-hour mass rate NO2





6.1.4.2 January 2025 - Monthly 1-hour mass rate NO

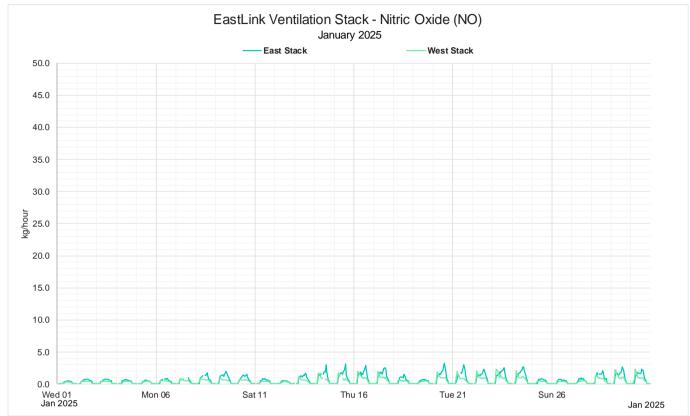


Figure 3: January 2025 Monthly 1-hour mass rate NO





6.1.4.3 January 2025 - Monthly 1-hour mass rate CO

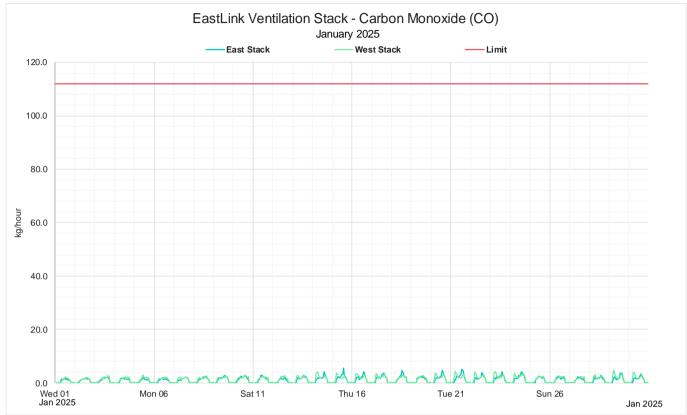


Figure 4: January 2025 Monthly 1-hour mass rate CO





6.1.4.4 January 2025 - Monthly 1-hour mass rate PM_{2.5}

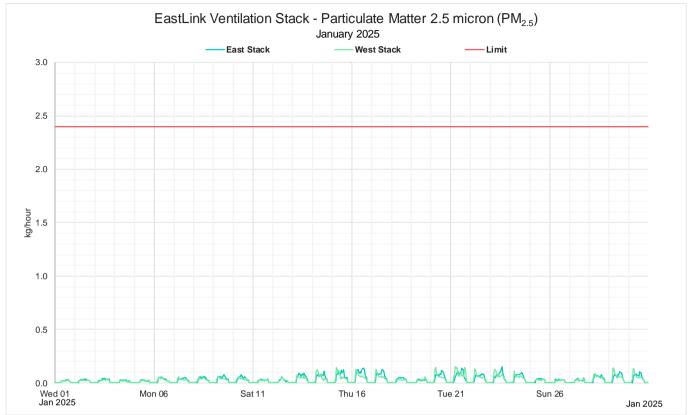


Figure 5: January 2025 Monthly 1-hour mass rate PM_{2.5}





6.1.4.5 January 2025 - Monthly 1-hour mass rate PM₁₀


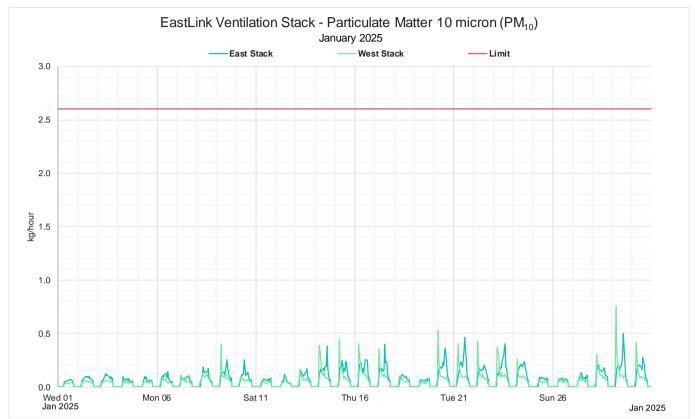



Figure 6: January 2025 Monthly 1-hour mass rate PM10





6.1.4.6 January 2025 - Monthly 1-hour average stack velocity

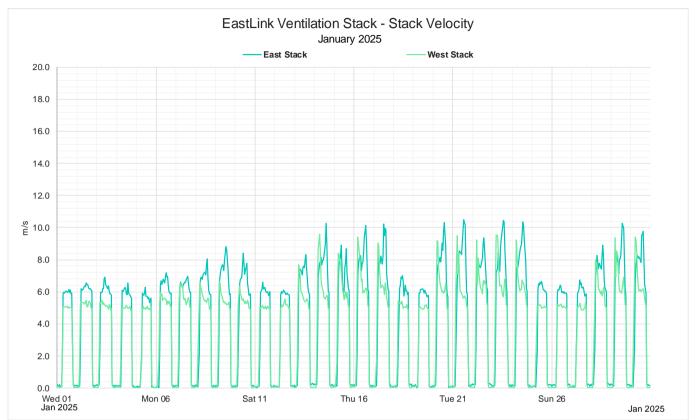







6.1.4.7 January 2025 - Monthly 1-hour average stack temperature

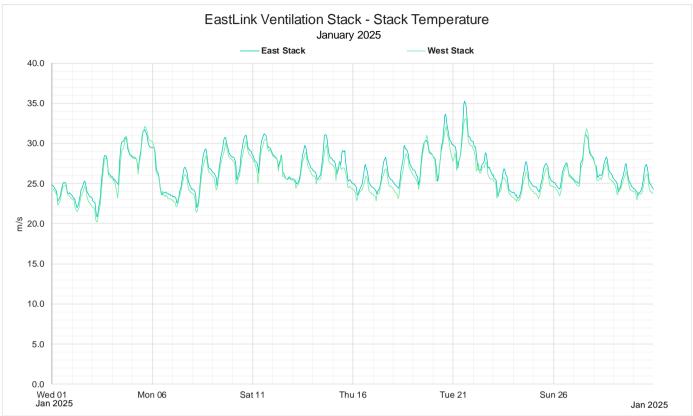


Figure 8: January 2025 Monthly 1-hour average stack temperature





6.1.5 Data Validation Table

Data validation details for the ventilation stack parameters are provided in the Table 18 and Table 19 below.

6.1.5.1 January 2025 - Western Ventilation Stack

	Eastlink Tunnel Western Ventilation Stack Data Validation January 2025									
Start Date	End Date	Parameters	Reason	Hours affected	User Name	Change Date				
1/01/2025 00:00	31/03/2025 23:59	со	Offset applied to data: Offset A: 0.0 Offset B: 0.5	N/A	TA	25/04/2025				
1/01/2025 03:37	30/01/2025 02:39	PM _{2.5} , PM ₁₀	Intermittent unrealistic data - negative	N/A	ТА	25/04/2025				
14/01/2025 10:47	14/01/2025 12:26	CO, NO, NO ₂ , NO _x	Maintenance	1.6	ТА	25/04/2025				

This table details any missing data, data removed due to being deemed invalid, or data that has been adjusted.

Table 18: January 2025 Western Ventilation Stack data validation

6.1.5.2 January 2025 - Eastern Ventilation Stack

Eastlink Tunnel Eastern Ventilation Stack Data Validation January 2025									
Start Date	End Date	Parameters	Reason	Hours affected	User Name	Change Date			
1/01/2025 00:00	7/01/2025 10:23	СО	Offset applied to data: Offset A: -0.5 Offset B: -0.5	N/A	ТА	25/04/2025			
3/01/2025 01:10	28/01/2025 02:32	PM _{2.5} , PM ₁₀	Intermittent unrealistic data - negative	N/A	ТА	25/04/2025			
5/01/2025 07:19	5/01/2025 07:20	CO, NO, NO ₂ , NO _x , PM _{2.5} , PM ₁₀	Data logger reboot	0.0	ТА	25/04/2025			
6/01/2025 08:58	6/01/2025 09:30	CO, NO, NO ₂ , NO _x	Maintenance	0.5	ТА	25/04/2025			
7/01/2025 10:24	7/01/2025 14:57	PM _{2.5} , PM ₁₀	Unrealistic data	4.5	ТА	25/04/2025			
7/01/2025 14:58	7/02/2025 09:37	СО	Offset applied to data: Offset A: -0.8 Offset B: -1.2	N/A	ТА	25/04/2025			
8/01/2025 09:52	8/01/2025 10:25	CO, NO, NO ₂ , NO _x	Maintenance	0.6	ТА	25/04/2025			
14/01/2025 08:56	14/01/2025 10:22	CO, NO, NO ₂ , NO _x	Maintenance	1.4	ТА	25/04/2025			
21/01/2025 08:44	21/01/2025 09:35	CO, NO, NO ₂ , NO _x	Maintenance	0.8	ТА	25/04/2025			
28/01/2025 06:38	28/01/2025 06:39	CO, NO, NO ₂ , NO _x , PM _{2.5} , PM ₁₀	Data logger reboot	0.0	ТА	25/04/2025			
28/01/2025 09:07	28/01/2025 09:54	CO, NO, NO ₂ , NO _x	Maintenance	0.8	ТА	25/04/2025			
31/01/2025 09:01	31/01/2025 09:48	CO, NO, NO ₂ , NO _x	Maintenance	0.8	ТА	25/04/2025			

This table details any missing data, data removed due to being deemed invalid, or data that has been adjusted.

Table 19: January 2025 Eastern Ventilation Stack data validation





6.2 February 2025

6.2.1 Data Availability

Data availability for the in the ventilation stack parameters are provided in Table 20 below. For further information on data availability please refer to section 6.1.5.

EastLink Ventilation Stack Data Availability February 2025									
Station		NO	NO ₂	со	PM _{2.5}	PM ₁₀	Stack Velocity	Stack Temp.	
Western	Data Availability	87.1%	87.1%	95.2%	98.5%	99.4%	100.0%	100.0%	
	Collected Periods	585	585	640	662	668	672	672	
	Available Periods	672	672	672	672	672	672	672	
Eastern	Data Availability	93.9%	93.9%	92.0%	99.4%	88.5%	99.7%	100.0%	
	Collected Periods	631	631	618	668	595	670	672	
	Available Periods	672	672	672	672	672	672	672	

Table 20: February 2025 ventilation stack data availability





6.2.2 Exceedances

Instances of the ventilation stack pollutants exceeding the EPA Limits goals during the reporting period are presented in Table 21 below. Maximum mass rates are provided for comparison to the limits.

EastLink Ventiliation Stack Air Quality Limit Exceedances February 2025										
Location	Parameter	Time Period	Licence Limit	Units	Maximum Mass Rate	Number of exceedances	Value of exceedance	Date and Time of exceedance		
Western Ventilation Stack (Discharge Point 1)	NO ₂	1-hour	3.98	kg/h	0.39	-	-	-		
	со	1-hour	112	kg/h	5.50	-	-	-		
	PM _{2.5}	1-hour	2.4	kg/h	0.21	-	-	-		
	PM ₁₀	1-hour	2.6	kg/h	0.82	-	-	-		
Eastern Ventilation Stack (Discharge Point 2)	NO ₂	1-hour	3.98	kg/h	0.96	-	-	-		
	со	1-hour	112	kg/h	6.82	-	-	-		
	PM _{2.5}	1-hour	2.4	kg/h	0.16	-	-	-		
	PM ₁₀	1-hour	2.6	kg/h	0.75	-	-	-		

There were nil exceedances of the prescribed limits during the reporting period.

Table 21: February 2025 Exceedances of EPA Goals





6.2.3 Tabulated Results

6.2.3.1 Statistical Summary of 1-hour Mass Rate Data Western and Eastern Ventilation Stacks

Table 22 presents 1-hour mass rate statistical data for the Western and Eastern ventilation stacks.

1-hour mass rates are calculated from 1 minute average data.

EastLink Ventilation Stack Summary February 2025								
Location	Parameter	Maximum	99 th Percentile	98 th Percentile	95 th Percentile	90 th Percentile	75 th Percentile	50 th Percentile
Western Ventilation Stack	NO (kg/h)	2.62	2.25	2.14	1.73	1.33	0.94	0.44
	NO ₂ (kg/h)	0.39	0.35	0.32	0.27	0.23	0.17	0.11
	CO (kg/h)	5.50	4.63	4.35	3.93	3.45	2.59	1.74
	PM _{2.5} (kg/h)	0.2	0.2	0.2	0.1	0.1	0.1	0.0
	PM ₁₀ (kg/h)	0.8	0.5	0.4	0.3	0.2	0.1	0.1
Eastern Ventilation Stack	NO (kg/h)	3.63	3.24	3.06	2.55	2.18	1.54	0.57
	NO ₂ (kg/h)	0.96	0.82	0.78	0.62	0.48	0.30	0.15
	CO (kg/h)	6.82	5.38	4.94	4.13	3.35	2.34	1.48
	PM _{2.5} (kg/h)	0.2	0.1	0.1	0.1	0.1	0.1	0.0
	PM ₁₀ (kg/h)	0.7	0.4	0.4	0.3	0.3	0.2	0.1

Table 22: February 2025 Summary of 1-hour mass rate pollutant data





6.2.4 Graphical Representations

The following charts present 1-hour mass rate data for NO, NO₂, CO, PM_{2.5}, PM₁₀ and Stack Velocity for the Western and Eastern ventilation stacks.

1-hour mass rates are calculated from 1 minute average data.

6.2.4.1 February 2025 - Monthly 1-hour mass rate NO₂

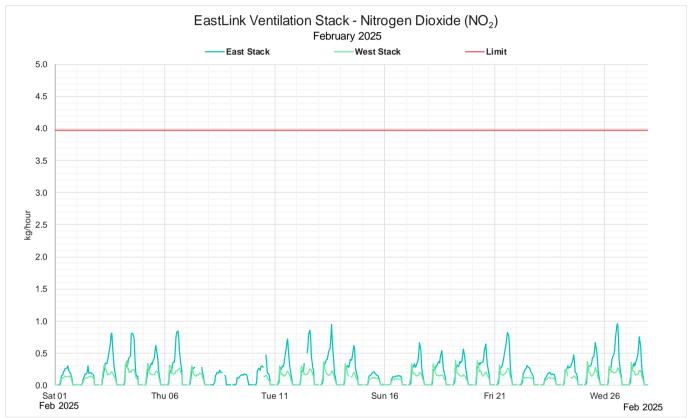


Figure 9: February 2025 Monthly 1-hour mass rate NO2





6.2.4.2 February 2025 - Monthly 1-hour mass rate NO

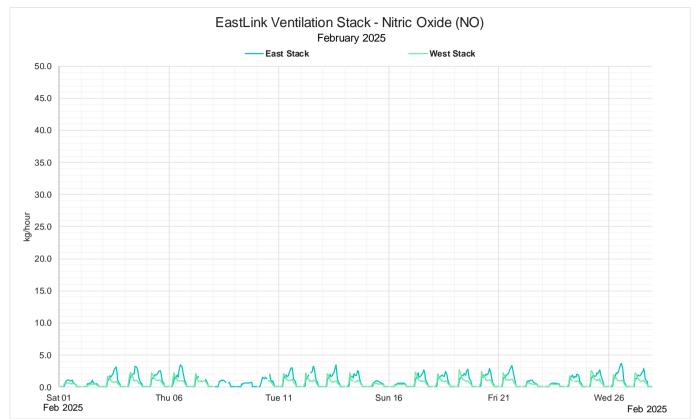


Figure 10: February 2025 Monthly 1-hour mass rate NO





6.2.4.3 February 2025 - Monthly 1-hour mass rate CO

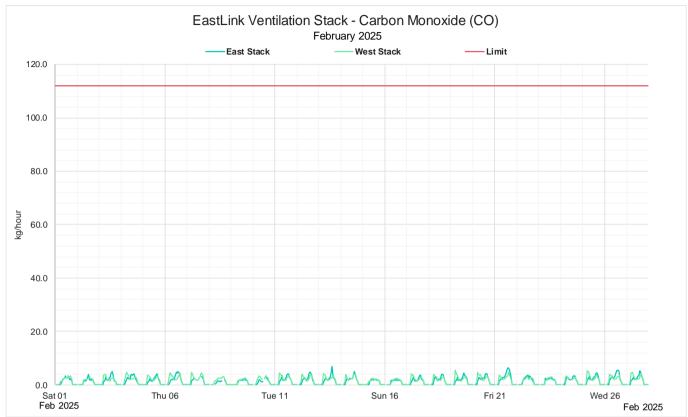


Figure 11: February 2025 Monthly 1-hour mass rate CO





6.2.4.4 February 2025 - Monthly 1-hour mass rate PM_{2.5}

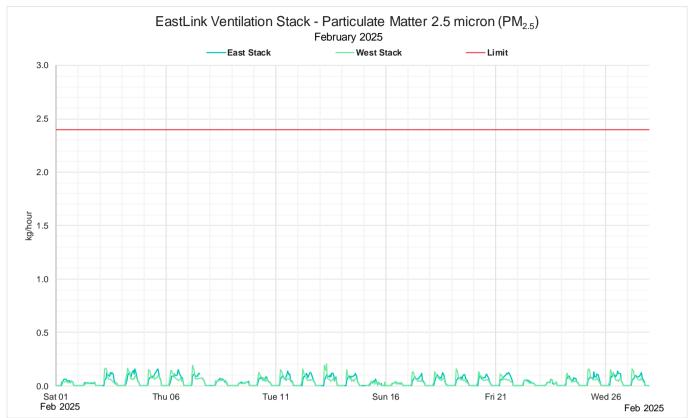


Figure 12: February 2025 Monthly 1-hour mass rate PM2.5





6.2.4.5 February 2025 - Monthly 1-hour mass rate PM₁₀


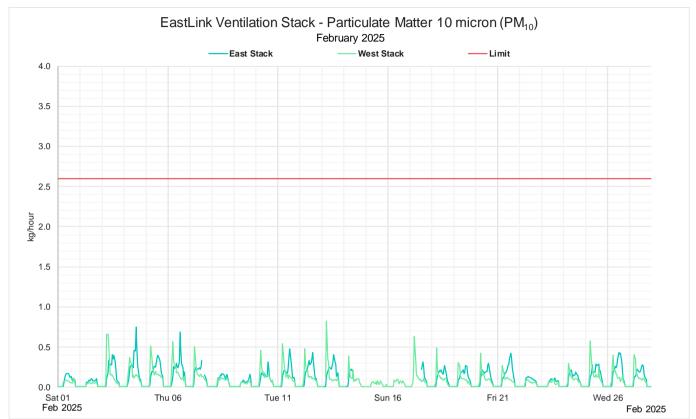



Figure 13: February 2025 Monthly 1-hour mass rate PM10





6.2.4.6 February 2025 - Monthly 1-hour average stack velocity

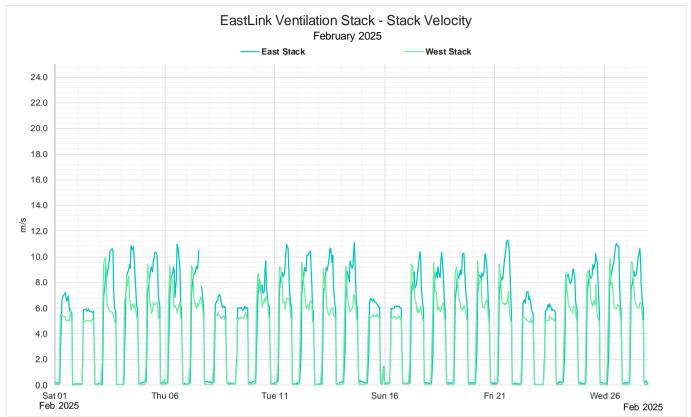







6.2.4.7 February 2025 - Monthly 1-hour average stack temperature

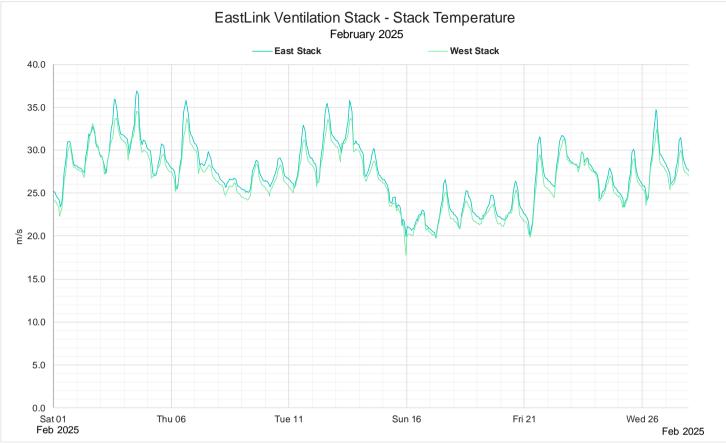


Figure 15: February 2025 Monthly 1-hour average stack temperature





6.2.5 Data Validation Table

Data validation details for the ventilation stack parameters are provided in the Table 23 and Table 24 below.

6.2.5.1 February 2025 - Western Ventilation Stack

	Eastlink Tunnel Western Ventilation Stack Data Validation February 2025							
Start Date	End Date	Parameters	Reason	Hours affected	User Name	Change Date		
1/02/2025 00:12	28/02/2025 23:28	PM _{2.5} , PM ₁₀	Intermittent unrealistic data - negative	N/A	ТА	25/04/2025		
3/02/2025 01:46	8/02/2025 01:00	NO, NO ₂ , NO _x	Multiplier applied to data: Multiplier A: 1.093454 Multiplier B: 1.093454	N/A	ТА	25/04/2025		
8/02/2025 01:46	10/02/2025 11:09	NO, NO ₂ , NO _x	Calibration out of tolerance	57.4	ТА	25/04/2025		
10/02/2025 11:10	10/02/2025 11:47	CO, NO, NO ₂ , NO _x	Maintenance	0.6	ТА	25/04/2025		
10/02/2025 11:48	14/02/2025 10:19	NO, NO ₂ , NO _x	Multiplier applied to data: Multiplier A: 0.999382 Multiplier B: 0.882642	N/A	ТА	25/04/2025		
14/02/2025 10:20	14/02/2025 10:44	CO, NO, NO ₂ , NO _x	Maintenance	0.4	ТА	25/04/2025		
22/02/2025 01:46	24/02/2025 09:36	NO, NO ₂ , NO _x	Multiplier applied to data: Multiplier A: 0.889439 Multiplier B: 0.889439	N/A	ТА	25/04/2025		
24/02/2025 09:36	24/02/2025 10:59	CO, NO, NO ₂ , NO _x	Maintenance	1.4	ТА	25/04/2025		

This table details any missing data, data removed due to being deemed invalid, or data that has been adjusted. Table 23: February 2025 Western Ventilation Stack data validation





6.2.5.2 February 2025 - Eastern Ventilation Stack

	Eastlink Tunnel Eastern Ventilation Stack Data Validation February 2025						
Start Date	End Date	Parameters	Reason	Hours affected	User Name	Change Date	
2/02/2025 22:10	28/02/2025 08:33	PM _{2.5} , PM ₁₀	Intermittent unrealistic data - negative	N/A	ТА	25/04/2025	
7/02/2025 09:38	7/02/2025 15:36	CO, NO, NO ₂ , NO _x	Maintenance	6.0	ТА	25/04/2025	
7/02/2025 14:27	7/02/2025 15:36	PM _{2.5} , PM ₁₀	Maintenance	1.2	ТА	25/04/2025	
8/02/2025 01:13	8/02/2025 08:08	CO	Intermittent unrealistic data - negative	N/A	ТА	25/04/2025	
8/02/2025 15:35	8/02/2025 16:34	CO, NO, NO ₂ , NO _x	Maintenance	1.0	ТА	25/04/2025	
10/02/2025 12:12	10/02/2025 12:56	CO, NO, NO ₂ , NO _x	Maintenance	0.7	ТА	25/04/2025	
10/02/2025 13:12	10/02/2025 13:49	CO, NO, NO ₂ , NO _x	Maintenance	0.6	ТА	25/04/2025	
12/02/2025 08:51	12/02/2025 10:27	CO, NO, NO ₂ , NO _x	Maintenance	1.6	ТА	25/04/2025	
14/02/2025 10:16	17/02/2025 12:41	PM ₁₀	Maintenance	74.4	ТА	25/04/2025	
15/02/2025 02:14	5/03/2025 14:57	со	Multiplier applied to data: Multiplier A: 1.0 Multiplier B: 0.935660	N/A	TA	25/04/2025	
15/02/2025 19:18	16/02/2025 04:28	CO	Intermittent unrealistic data - negative	N/A	ТА	25/04/2025	
19/02/2025 02:14	5/03/2025 14:57	со	Offset applied to data: Offset A: 0.0 Offset B: -1.0	N/A	ТА	25/04/2025	
24/02/2025 09:05	24/02/2025 09:19	CO, NO, NO ₂ , NO _x	Maintenance	0.2	ТА	25/04/2025	

This table details any missing data, data removed due to being deemed invalid, or data that has been adjusted.

Table 24: February 2025 Eastern Ventilation Stack data validation





6.3 March 2025

6.3.1 Data Availability

Data availability for the in the ventilation stack parameters are provided in Table 25 below. For further information on data availability please refer to section 6.2.5

	EastLink Ventilation Stack Data Availability March 2025							
Station		NO	NO ₂	со	PM _{2.5}	PM ₁₀	Stack Velocity	Stack Temp.
Western	Data Availability	95.7%	95.7%	95.7%	91.8%	100.0%	100.0%	99.9%
	Collected Periods	712.0	712.0	712.0	683.0	744.0	744.0	743.0
	Available Periods	744.0	744.0	744.0	744.0	744.0	744.0	744.0
	Data Availability	95.3%	95.3%	95.3%	96.0%	96.2%	100.0%	100.0%
Eastern	Collected Periods	709	709	709	714	716	744	744
	Available Periods	744	744	744	744	744	744	744

Table 25: March 2025 ventilation stack data availability





6.3.2 Exceedances

Instances of the ventilation stack pollutants exceeding the EPA Limits goals during the reporting period are presented in Table 26 below. Maximum mass rates are provided for comparison to the limits.

	EastLink Ventiliation Stack Air Quality Limit Exceedances March 2025								
Location	Parameter	Time Period	Licence Limit	Units	Maximum Mass Rate	Number of exceedances	Value of exceedance	Date and Time of exceedance	
10/	NO ₂	1-hour	3.98	kg/h	0.41	-	-	-	
Western Ventilation Stack	со	1-hour	112	kg/h	5.50	-	-	-	
(Discharge Point 1)	PM _{2.5}	1-hour	2.4	kg/h	0.30	-	-	-	
1 On CT	PM ₁₀	1-hour	2.6	kg/h	0.82	-	-	-	
Frater	NO ₂	1-hour	3.98	kg/h	0.98	-	-	-	
Eastern Ventilation	со	1-hour	112	kg/h	6.51	-	-	-	
Stack (Discharge Point 2)	PM _{2.5}	1-hour	2.4	kg/h	0.20	-	-	-	
1 0/11 2)	PM ₁₀	1-hour	2.6	kg/h	0.48	-	-	-	

There were nil exceedances of the prescribed limits during the reporting period.

Table 26: March 2025 Exceedances of EPA Goals





6.3.3 Tabulated Results

6.3.3.1 Statistical Summary of 1-hour mass rate data Western and Eastern Ventilation Stacks

Table 27 presents 1-hour mass rate statistical data for the Western and Eastern ventilation stacks.

1-hour mass rates are calculated from 1 minute average data.

	EastLink Ventilation Stack Summary March 2025							
Location	Parameter	Maximum	99 th Percentile	98 th Percentile	95 th Percentile	90 th Percentile	75 th Percentile	50 th Percentile
	NO (kg/h)	2.38	2.19	2.05	1.72	1.26	0.91	0.43
	NO ₂ (kg/h)	0.41	0.35	0.32	0.25	0.21	0.15	0.09
Western Ventilation Stack	CO (kg/h)	5.50	4.79	4.47	4.04	3.50	2.63	1.75
	PM _{2.5} (kg/h)	0.3	0.1	0.1	0.1	0.1	0.0	0.0
	PM ₁₀ (kg/h)	0.8	0.5	0.4	0.2	0.2	0.1	0.0
	NO (kg/h)	3.73	2.94	2.86	2.40	2.04	1.40	0.55
	NO ₂ (kg/h)	0.98	0.72	0.66	0.56	0.42	0.27	0.14
Eastern Ventilation Stack	CO (kg/h)	6.51	5.60	5.08	4.43	3.36	2.48	1.68
	PM _{2.5} (kg/h)	0.2	0.1	0.1	0.1	0.1	0.1	0.0
	PM ₁₀ (kg/h)	0.5	0.4	0.4	0.3	0.2	0.2	0.1

Table 27: March 2025 Summary of 1-hour mass rate pollutant data





6.3.4 Graphical Representations

The following charts present 1-hour mass rate data for NO, NO₂, CO, PM_{2.5}, PM₁₀ and Stack Velocity for the Western and Eastern ventilation stacks.

1-hour mass rates are calculated from 1 minute average data.

6.3.4.1 March 2025 - Monthly 1-hour mass rate NO₂

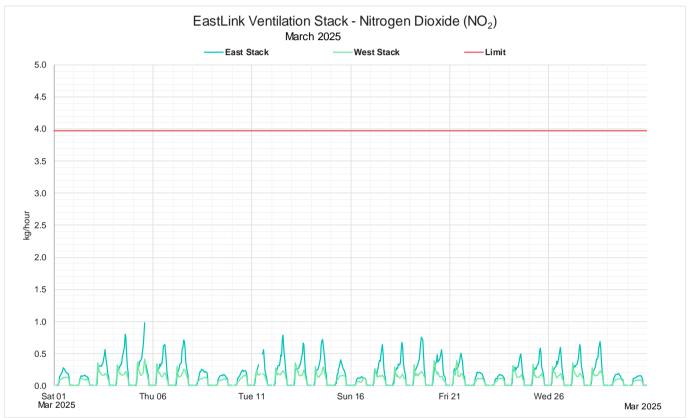


Figure 16: March 2025 Monthly 1-hour mass rate NO2





6.3.4.2 March 2025 - Monthly 1-hour mass rate NO

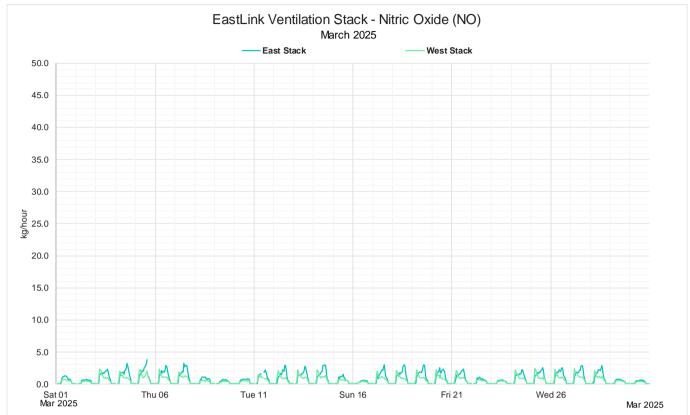


Figure 17: March 2025 Monthly 1-hour mass rate NO





6.3.4.3 March 2025 - Monthly 1-hour mass rate CO

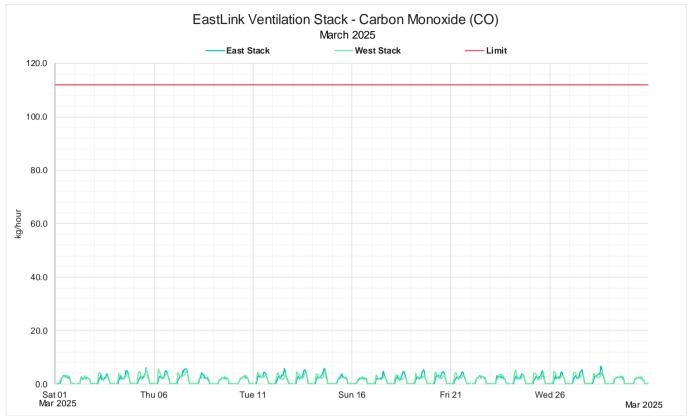


Figure 18: March 2025 Monthly 1-hour mass rate CO





6.3.4.4 March 2025 - Monthly 1-hour mass rate PM_{2.5}

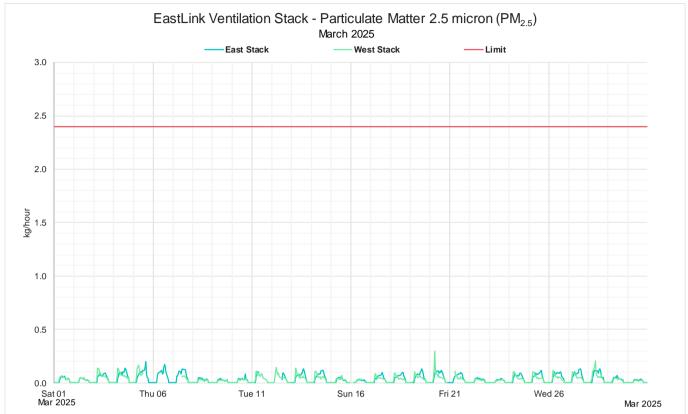


Figure 19: March 2025 Monthly 1-hour mass rate PM_{2.5}





6.3.4.5 March 2025 - Monthly 1-hour mass rate PM₁₀

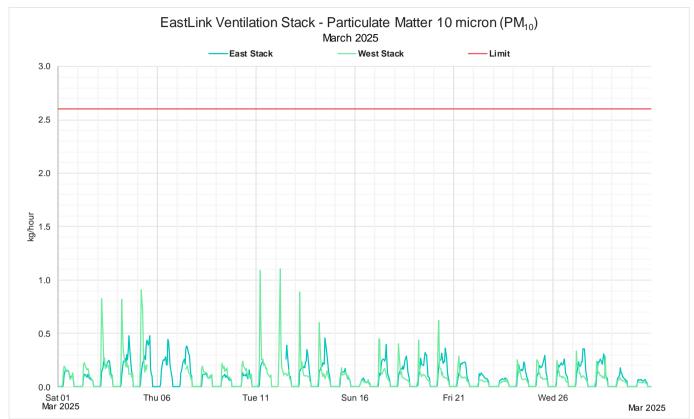


Figure 20: March 2025 Monthly 1-hour mass rate PM10





6.3.4.6 March 2025 - Monthly 1-hour average stack velocity

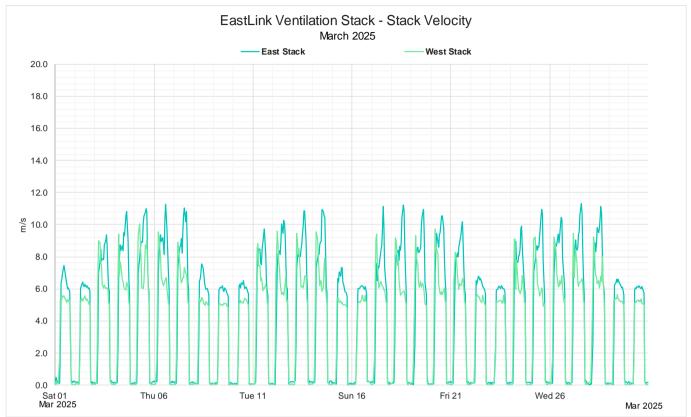


Figure 21: March 2025 Monthly 1-hour average stack velocity





6.3.4.7 March 2025 - Monthly 1-hour average stack temperature

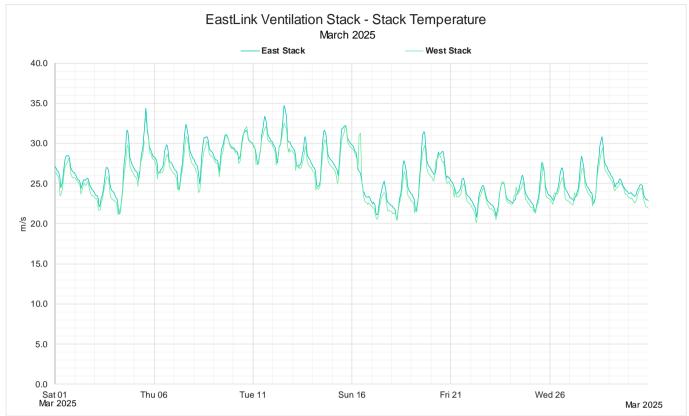


Figure 22: March 2025 Monthly 1-hour average stack temperature





6.3.5 Data Validation Table

Data validation details for the ventilation stack parameters are provided in the Table 28 and Table 29 below.

6.3.5.1 March 2025 - Western Ventilation Stack

	Eastlink Tunnel Western Ventilation Stack Data Validation March 2025							
Start Date	End Date	Parameters Reason		Hours affected	User Name	Change Date		
1/03/2025 00:36	31/03/2025 23:24	PM _{2.5} , PM ₁₀	Intermittent unrealistic data - negative	N/A	ТА	25/04/2025		
5/03/2025 13:17	7/03/2025 10:48	PM _{2.5} , PM ₁₀	Maintenance	45.5	ТА	25/04/2025		
11/03/2025 11:59	11/03/2025 12:51	CO, NO, NO ₂ , NOx	Maintenance	0.9	TA	25/04/2025		
20/03/2025 22:01	21/03/2025 05:38	PM _{2.5} , PM ₁₀	Unrealistic data - excessive noise	7.6	TA	25/04/2025		

This table details any missing data, data removed due to being deemed invalid, or data that has been adjusted. Table 28: March 2025 Western Ventilation Stack data validation

6.3.5.2 March 2025 - Eastern Ventilation Stack

Eastlink Tunnel Eastern Ventilation Stack Data Validation March 2025								
Start Date	End Date	Parameters	Reason	Hours affected	User Name	Change Date		
5/03/2025 14:58	5/03/2025 15:17	CO, NO, NO ₂ , NOx	Maintenance	0.3	ТА	25/04/2025		
6/03/2025 22:27	28/03/2025 04:17	PM _{2.5} , PM ₁₀	Intermittent unrealistic data - negative	N/A	ТА	25/04/2025		
11/03/2025 09:20	11/03/2025 11:33	CO, NO, NO ₂ , NO _x	Maintenance	2.2	ТА	25/04/2025		
11/03/2025 09:20	12/03/2025 12:03	PM _{2.5} , PM ₁₀	Maintenance	26.7	ТА	25/04/2025		
15/03/2025 02:14	31/03/2025 23:59	СО	Offset applied to data: Offset A: 0.0 Offset B: -0.4	N/A	ТА	25/04/2025		

This table details any missing data, data removed due to being deemed invalid, or data that has been adjusted.

Table 29: March 2025 Eastern Ventilation Stack data validation





6.4 Data Availability Year to Date

Data availability statistics for year to date (01 January 2025 to 31 March 2025) are provided in Table 30 below:

EastLink Ventilation Stack Data Availability January 2025 to March 2025							
Station	NO	NO ₂	со	PM _{2.5}	PM ₁₀	Stack Velocity	Stack Temp.
Western	92.7%	92.7%	95.4%	<mark>9</mark> 6.7%	99.8%	100.0%	100.0%
Eastern	94.4%	94.4%	<mark>93.8%</mark>	98.4%	94.9%	99.9%	100.0%

Table 30: EastLink Ventilation Stack year to date data availability






6.5 Annual Performance Statement Bubble Limits


The EPA License 2043 Condition LI_DA1 designates annual emission rate bubble limits for discharge points 1 and 2. Annual emission rates are calculated from 1st July to 30th June each year to coincide with the Annual Performance Statement (APS) reporting period. Ventilation Stack emission rates year to date (01 July 2024 to 31 March 2025) are shown in Table 31 below.

EastLink Ve	EastLink Ventilation Stack Mass Rate July 2024 to March 2025					
Location	NO ₂	СО	PM _{2.5}	PM ₁₀		
Location	Tonnes	Tonnes	Tonnes	Tonnes		
Western Ventilation Stack (Discharge Point 1)	0.595	9.447	0.183	0.407		
Eastern Ventilation Stack (Discharge Point 2)	0.973	8.714	0.220	0.533		
Total	1.568	18.161	0.403	0.940		
Percentage of Licence limit	4.5%	1.9%	1.9%	4.1%		
Annual Limit (Tonnes)	35	980	21	23		

Table 31: Annual Performance Statement stack emission rates

Figure 23 below presents the ventilation stack emissions of each parameter as a percentage of the Licence limit compared with the percentage of elapse APS Reporting period.

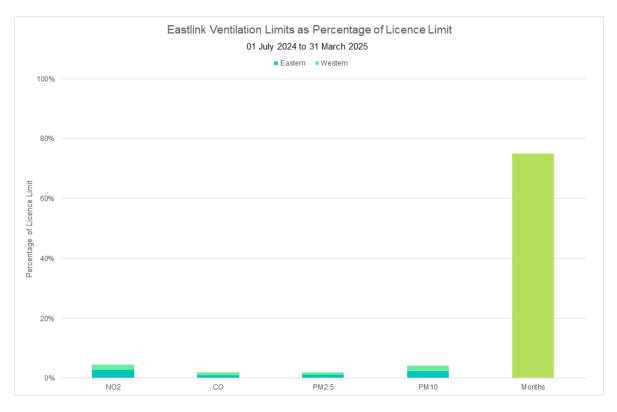







7 Report Summary

• There were nil exceedances of the prescribed limits during the reporting period.





Appendix 1

Glossary

The following terms and abbreviations are used in this report

CO	Carbon monoxide
DP1	Discharge Point 1
DP2	Discharge Point 2
kg/hour	Kilograms per hour
g/5m	Grams per 5 minutes
m³/s	Cubic meters per second
mg/m³	Milligrams per cubic meter at dry, standard temperature and pressure (0°C and 101.3 kPa)
NO	Nitric oxide
NO ₂	Nitrogen dioxide
PM ₁₀	Particulate less than 10 microns in equivalent aerodynamic diameter
PM _{2.5}	Particulate less than 2.5 microns in equivalent aerodynamic diameter

Data Validation Explanations

Automatic background check refers to when analyser samples zero air and measures the level of the concentration voltage. This voltage is taken as the zero signal level and this value is subtracted from any subsequent readings as an active zero compensation. This is the analyser's fine zero measurement.

Calibration check outside tolerance refers to when the calibration values are outside the tolerance limits set for the precision check.

Offset or Multiplier Applied to data refers to an offset or multiplier applied to the data. This operation may be performed for a number of reasons including: (a) when a clear trend / drift outside the tolerance limit can be demonstrated by repeated operation precision checks, (b) when a correction is required on previously logged data due to a calibration check being outside the allowable tolerance

Data transmission error refers to a period of time when the instrument could not transmit data. This may be due to a communication fault between the logger and instrument.

Equipment malfunction/instrument fault refers to a period of time when the instrument was not in the normal operating mode and did not measure a representative value of the existing conditions.

Missing data/data not available refers to a period of time when either data has been lost or could not be collected.

Instrument Alarm refers to an alarm produced by the instrument. A range of alarms can be produced depending on how operation of the instrument is being affected.

Instrument out of service refers to an unavailability of data due to an instrument being shut down for repair, maintenance, or factory calibration.





Logger error refers to when an error occurs and instrument readings are not correctly recorded by the logger.

Maintenance refers to a period of time when the logger / instrument was unavailable due to maintenance.

Overnight span/zero out of tolerance refers to when the span/zero reading measured by the analyser during an automatic precision check falls outside of the expected concentration limits.

Power Interruption refers to no power to the station therefore no data was collected at this time.

Remote Calibration refers to when a technician remotely connects to the station and manually performs a span check.

Warm up after power interruption refers to the start up period of an instrument after power has been restored.

